


Course: Individual Software Development Process 2026

Iteration Report: Iteration 2

By Left4Dead

Chosen Irl Challenge: Project D: Course Support & Activity Dashboard

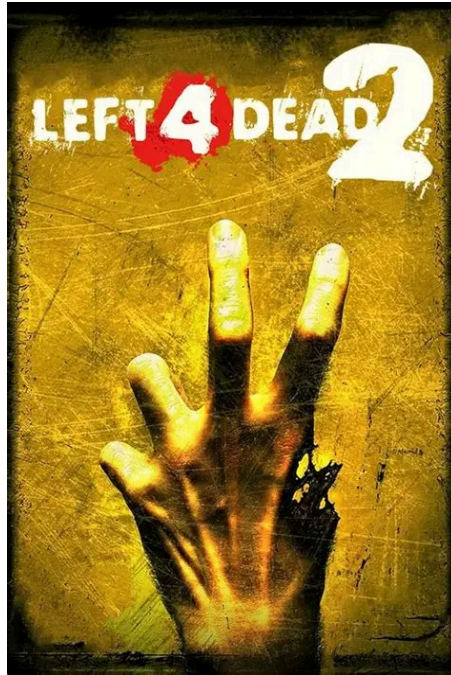

Thanawin Thanapornthawan	6810545654
Phutarak Wongpitak	6810545841
Pakhin Daonan	6810545859
Kantanat Utamapongchai	6810545468

Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	2
2. Sprint/Board Status Snapshot.....	2
3. Scope Addition/Change Log.....	4
4. Retrospective.....	5
5. Testing & Quality Notes.....	5
6. Project Risk Register.....	6
7. Individual Contribution Log.....	6


1. Project Snapshot

Note: This section must include both the Gantt chart for the whole project and the calculation of the critical path for the project and each iteration. Created via Plane.so.

Note: Project Repository is mandatory for the report submission of Iteration 2. For Iteration 1, this can be left blank as "(WIP)".

Project Repository: [ThanawinTH/ISP-Left4Dead](#)


1.1 Project-Wide Gantt Chart

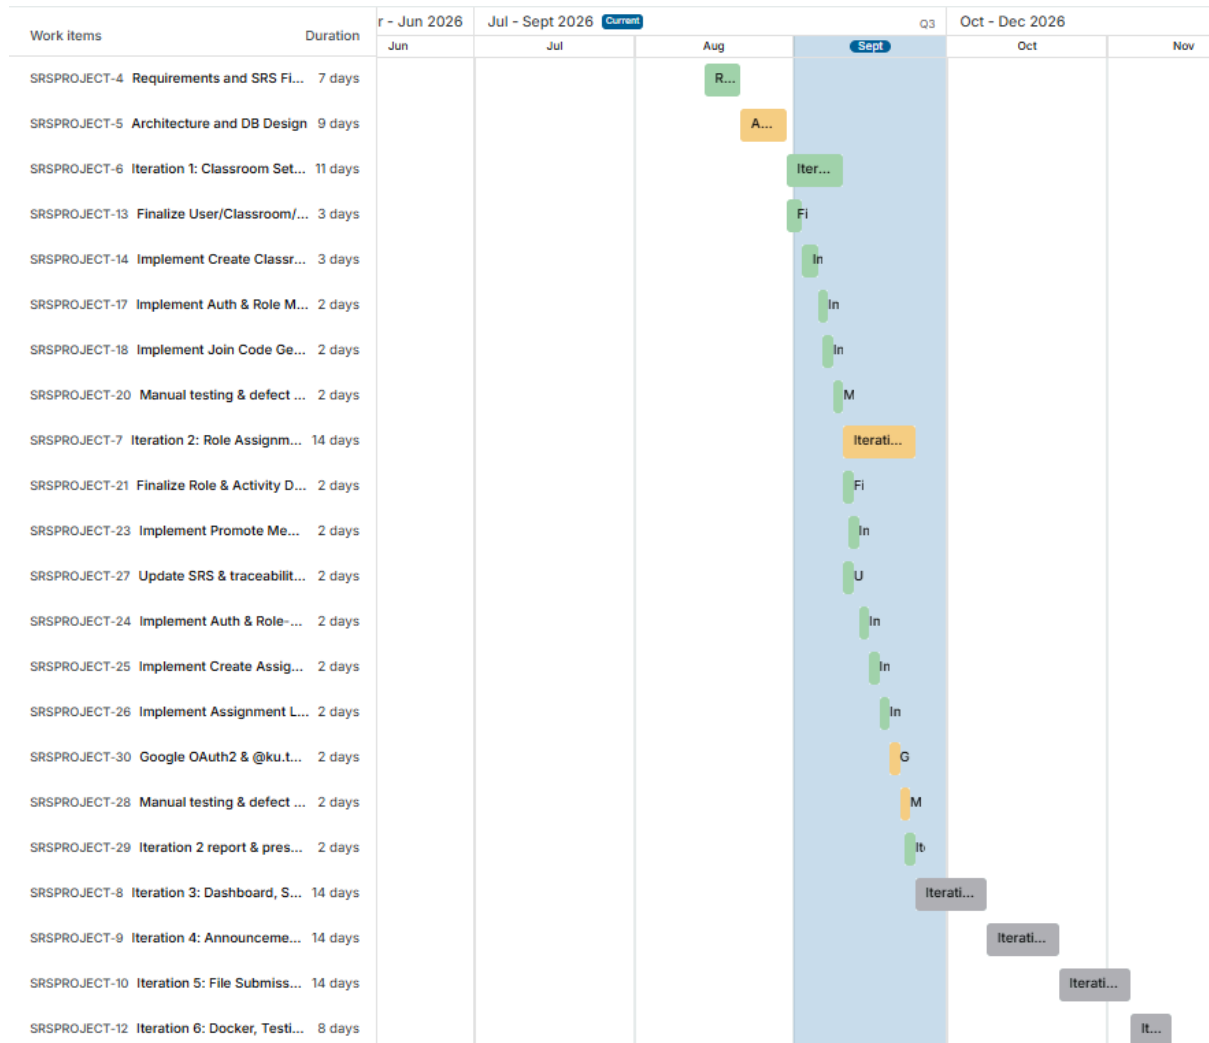

Critical Path: Requirements and SRS Finalization → Architecture and DB Design → Iteration 1: Classroom Setup & Membership (US-1, US-2, US-3) → Iteration 2: Role Assignment, Activity Management, Google OAuth2 & @ku.th Restriction (US-4, US-5, US-6, US-16) → Iteration 3: Dashboard, Schedule & At-Risk (US-7, US-8, US-9) → Iteration 4: Announcements & Staff Channel (US-10-US-13) → Iteration 5: File Submission & Status (US-14, US-15) → Iteration 6: Docker, Testing & Deployment

Critical Path Duration: 98 calendar days

1.2 Current Iteration Gantt Chart

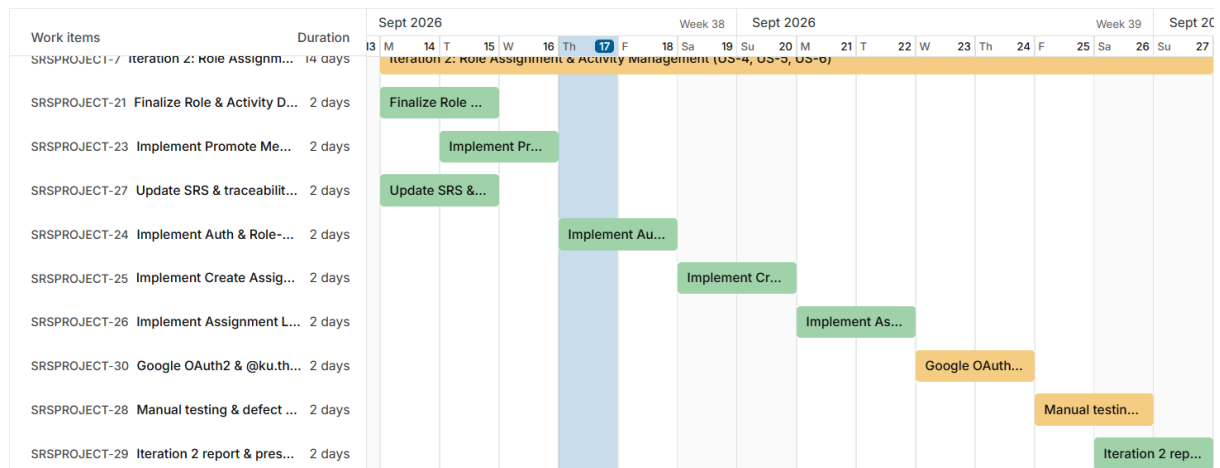

Critical Path: Finalize Role & Activity DB schema, Update SRS & traceability matrix → Implement Promote Member Role (US-4) → Implement Auth & Role-Based Access Control (SRS-7) → Implement Create Assignment (US-5) → Implement Assignment List & Visibility (SRS-13, SRS-14) → Google OAuth2 & @ku.th Restriction (US-16) → Manual testing & defect fixes

Critical Path Duration: 14 calendar days

2. Sprint/Board Status Snapshot

Note: User stories must be consistent with the user stories in Software Proposal (Week 4). For Maximum Capacity, It Must Be:

- 3 User Stories for Iteration 1
- 4 User Stories for Iteration 2

Iteration Goal: Deliver a working role assignment and activity management slice so that a lecturer can promote classroom members to TA or university staff, while authorized staff can create activities and update their status. This iteration directly supports Sub-Goals SG-1 and SG-2 from the SRS.

Capacity Declared: 4 user stories (maximum capacity for Iteration 2).

User Story	Description	Owner	Status	Within Capacity(Y/N)	Notes
US-4	As a lecturer, I want to promote a member to TA or university staff so that only the people I trust can change course activities.	Pakhin Daonan, Thanawin Thanapornthawan	In Progress	Y	The backend implements the role column in memberships, the promote endpoint, and permission checks. The front end provides the member page with a role dropdown. Covers SRS-6 and

					SRS-7.
US-5	As an administrator, I want to create a menu item.	Phutarak Wongpitak , Thanawin Thanapornthawan	In Progress	Y	The backend implements the assignments table, and POST creates the endpoint. The front end implements the Create Assignment form. Covers SRS-8, SRS-9, SRS-10 and SRS-11.
US-6	As an administrator, I want to update menu item availability.	Phutarak Wongpitak , Kantanut Utamapongchai	In Progress	Y	The backend implements the PATCH endpoint for updating activity status. Front end implements the status control. Covers SRS-8 and SRS-11.
US-16	As a student, lecturer, TA, or university staff, I want only Kasetsart University members to be able to log in so that classroom data stays within the university.	Not yet	Deferred	N	The team has not yet agreed to include US-16 in Iteration 2. The story may be postponed to a later iteration after the team discusses the schedule and workload.

3. Scope Addition/Change Log

Note: Log any item added, expanded, or swapped in after planning began. Empty is a good sign; frequent entries signal scope creep.

Item added/changed	Reason	What was dropped to compensate (one-in-one-out)?
Changed the term "activity" to "assignment" in the relevant user stories and clarified the assignment scope.	The term "activity" was too broad and could make the project scope unclear. "Assignment" better represents the functionality designed in the Figma interface and the intended use of the system.	None. This was a clarification of an existing user story rather than an additional user story.
US-5 and US-6 were refined to focus mainly on the lecturer creating and updating assignments.	The lecturer should have the authority to decide and manage assignment requirements, while TAs are responsible for checking students' submissions rather than deciding the assignment itself.	None. This refines the responsibility of an existing user story rather than adding new scope.
Assignment information was expanded to include title, description, due date, and the assigned TA responsible for checking the submission.	The additional fields were clarified from the Figma design so that an assignment contains the information needed for the lecturer to manage the work and its checking responsibility.	None. The fields refine the existing assignment-management functionality.
Separated TA and University staff into two distinct roles instead of treating them as one combined role.	The two roles may have different responsibilities and work sequences in the course. Separating them gives the system clearer role boundaries and allows their permissions and tasks to be managed independently.	None—this is a refinement of the existing role model rather than an additional user-facing feature.

4. Retrospective

What went well	What didn't go well	Action items for next sprint
The team divided the work clearly between backend and frontend. Each member knew what they were responsible for.	US-3 validation logic (rejecting invalid availability changes) was rushed near the deadline and left with only basic checks	Allocate more time to validation logic in Iteration 2; do not treat it as a "quick add-on" to a story
The team worked together on US-4, US-5, and US-6 and connected the frontend with the backend.	Underestimated how long UI polish would take for the customer-facing menu view	Reserve a fixed UI-polish buffer in future sprint planning rather than treating it as leftover time
The team followed the SRS and user stories when developing the features.	US-16 (Google OAuth2) was not yet agreed to be included in this iteration, so its schedule is still unclear.	Discuss US-16 early and decide whether to include it or move it to a later iteration.
The team was able to work together and adjust the system when the requirements changed.	Many parts of the requirements changed because the original scope was not clear enough, causing some work to be changed again	Make sure the requirements and design are clear and agreed on before starting development.

5. Testing & Quality Notes

Note: any bugs, defects, tests (informal & formal) encountered and/or fixed during this iteration can be included here. If there is none, just put "(None applicable)" below.

- A user is assigned as the TA responsible for an assignment. When the Lecturer changes that user's role from **TA to University Staff**, the system does not remove or update their previous TA assignment. The assignment still appears under them as a TA.
- **Join code without "-" is rejected.** The system rejects a join code when the - separator is omitted, even though the interface describes the code as a 6-digit PIN then this is fixed.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	Some tasks depend on other tasks and may cause delays.	M	M	Start important tasks early and tell the team when blocked	Open
R-02	The team is still learning backend development, so tasks may take longer.	M	M	Help each other and learn before starting difficult tasks. for future planning	Open
R-03	Frontend and backend may not work together correctly.	M	H	Test the API with the frontend early.	Open

7. Individual Contribution Log

Note: One row per member, filled in by that member. The submission of this file considered that the form below is consented and confirmed by the whole team. This section directly supports the Individual Project Contribution and Peer Evaluation grading components.

Note 2: For Iteration 1, evidence can be a reference to the video presentation/iteration report that is related to the responsible task(s) (e.g. Lalita's Evidence). However, for Iteration 2, the reference must be on **GitHub** file and commit only, which is uploaded by that team member.

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Pakhin Daonan	US-4 backend — role enum, member list and role-change endpoints, per-request permission checks	Authorisation check before an action; the role is read from the database on every request rather than cached in the	members.js, auth.js Commit code: 2c90d2f	5

		session, so a promotion applies without rejoining (SRS-7)		
Thanawin Thanapornthawan	US-4 front end — Members & Roles page; US-5 front end — Create Assignment form	Requirement-to-UI traceability; the form only offers what the server permits, and a rejected save rolls back	members.html, members.js commit code : c25b2d3 create-assignment.html, create-assignment.js commit code : 8a25313	5
Phutarak Wongpitak	US-5 and US-6 backend — assignments and assignment_staff tables, create, list and status-update endpoints	CRUD and database integrity; required fields and allowed values enforced in the schema as well as the handler	schema.sql, assignments.js commit code : 777dad0 routes.js commit code: ee1bf71	5
Kantanut Utamapongchai	US-6 front end — assignment list and status control; manual testing across US-4, US-5 and US-6	Testing against acceptance criteria including the negative cases — a student cannot reach the create page, a TA cannot create, an invalid due date is refused	schedule.js commit code: 3d63f22 and defect log	5
